Research methodology - Writing project proposals

Zoltán Horváth

Eötvös Loránd University
Faculty of Informatics
hz@inf.elte.hu

Nov. 1, 2022, ELTE

Contents

1. DoW - Description of Work
2. Work packages, tasks and deliverables
3. Project description

EU project proposals

Based on
- Standard application form: (https://ec.europa.eu/info/funding-tenders/opportunities/docs/2021-2027/horizon/temp-form/af/af_he-ria-ia_en.pdf),
- Successful FP 7 proposals
- A course: https://www.uniroma1.it/sites/default/files/allegati_notizie/Corso%2021e22_11_13%20Mecella.pdf
- A guide: (https://www.emdesk.com/de/guide/horizon-europe-proposal-writing-guide),
- Calls: https://research-and-innovation.ec.europa.eu/funding/funding-opportunities/funding-programmes-and-open-calls/horizon-europe_en

DoW - Description of Work

- Project summary;
- Project acronym
- Project full title;
- Project starting date and duration;
- One page abstract: motivation, results beyond the state of the art; entry month, exit month);
- List of participants (no., org.name, short name, country,
- Budget breakdown (RTD, MGT): personnel, subco, direct (travel, equip., other), indirect; Total and EU contribution;
- Personnel based on Person Month (PM);

Participants and budget

List of Beneficiaries

Project Number [1]	603121	Project Acronym [2]	DIVERSIFY

List of Beneficiaries

No	Name	Short name	Country	Project entry month[10]	Project exit month
-35	Hungarian Aquaculture Association	MASZ	Hungary	1	43
-17	NASJONALT INSTITUTT FOR ENAERINGS-OG SJOMATFORSKNING	NIFES	Norway	1	49
1	HELLENIC CENTRE FOR MARINE RESEARCH	HCMR	Greece	1	60
2	FUNDACION CANARIA PARQUE CIENTIFICO TECNOLOGICO DE LA UNIVERSIDAD DE LAS PALMAS DE GRAN CANARIA	FCPCT	Spain	1	60
3	INSTITUT DE RECERCA I TECNOLOGIA AGROALIMENTARIES.	IRTA	Spain	1	60
4	ISRAEL OCEANOGRAPHIC AND LIMNOLOGICAL RESEARCH LIMITED	IOLR	Israel	1	60
5	THE UNIVERSITY COURT OF THE UNIVERSITY OF ABERDEEN	UNIABDN	United Kingdom	1	60

RTD	*Personnel*		*€ 336,277*	*€ 212,039*	*€ 325,424*	*€ 235,817*	*€ 241,950*	*€ 177,555*
	Subcontracting		*€ 0*	*€ 0*	*€ 0*	*€ 0*	*€ 0*	*€ 0*
	Direct	Travel	€ 41,477	€ 25,277	€ 32,746	€ 25,500	€ 23,750	€ 22,419
		Equipment	€ 1,700	€ 30,000	€ 0	€ 2,500	€ 0	€ 12,500
		Other	€ 0	€ 0	€ 0	€ 0	€ 0	€ 0
		Total	*€ 43,177*	*€ 55,277*	*€ 32,746*	*€ 28,000*	*€ 23,750*	*€ 34,919*
	Indirect		*€ 227,672*	*€ 160,389*	*€ 26,737*	*€ 218,716*	*€ 159,420*	*€ 127,484*
		Total	**€ 607,126**	**€ 427,705**	**€ 384,907**	**€ 482,533**	**€ 425,120**	**€ 339,958**
EU Contribution			*€ 455,345*	*€ 320,778*	*€ 192,453*	*€ 361,900*	*€ 318,840*	*€ 254,969*

Work packages

LIST OF WORK PACKAGES (WP)

WP Number [53]	WP Title	Type of activity [54]	Lead beneficiary number [55]	Person-months [56]	Start month [57]	End month [58]
WP 1	Project Management	MGT	1	27.00	1	48
WP 2	Requirements & Assessment	COORD	2	42.00	1	10
WP 3	Sustainable network and use	COORD	1	41.00	3	48
WP 4	Dissemination and Communication	COORD	3	44.00	1	48
WP 5	Co-Design	RTD	4	2.00	11	26
WP 6	Prototyping	RTD	5	2.00	15	36
WP 7	Validation and testing	RTD	6	17.00	37	42
WP 8	Competitive Evaluation and Monitoring of the RTD work	COORD	6	48.00	11	42
			Total	223.00		

Delive-rable Number [61]	Deliverable Title	WP number [53]	Lead benefi-ciary number	Estimated indicative person-months	Nature [62]	Dissemi-nation level [63]	Delivery date [64]
D1.1	TEV and E. coli strains for robustness analysis	1	5	15.00	R	PU	12
D1.2	Analysis of robustness in TEV and E. coli	1	2	18.00	R	PU	20
D1.3	Analysis of evolvability (part 1)	1	5	16.00	R	PU	22
D1.4	Analysis of phenotypic innovation (part 1)	1	5	10.00	R	PU	24

Sum of PM of deliverables and of PM of participants are the same.

Work package description

- Total PM - assigned to participants;
- Start and End months;
- Objectives, e.g. "new high level parallel patterns";
- Description of work in set of paralell tasks - e.g. "T2.2: skeletons for multicore architectures";
- Phases, milestones (MS1, MS2, ..) and intertask, inter wokpackages dependencies;
- Responsibilities of participants for deliverables (D2.4), e,g, "ELTE will construct patterns in Erlang";
- Description of deliverables, e.g.:

"D2.2) Homogeneous Implementation of Initial Generic Patterns: Software Implementation of Initial Generic Patterns for Homogeneous Multicore Architectures, plus report. [month 12] "

Sum of PM of tasks = PM of workpackage;

PM distribution - Reports and review meetings

1. RTD/Innovation activities							
WP2	5.5	2	0	1	2	31	
WP3	11	25	0	1	8	10	
WP4	28.5	0	0	1	0	9	
WP5	0	3	9	1	14	9	

Tentative schedule of Project Reviews

Project Number	288570	Project Acronym	ParaPhrase
Review number	Tentative timing	Planned venue of review	Comments, if any
RV1	15	Brussels	First Annual Review
RV2	27	Brussels	Second Annual Review
RV3	42	Brussels	Final Review

Project description

- Concept and Project Objectives;
- Progress Beyond the State-of-the-Art;
- Success Criteria and Research Indicators;
- S/T (Science/Technology) Methodology and Associated Work Plan;
- Management Structure and Procedures;
- Beneficiaries;
- Consortium as a Whole;
- Strategic Impact;
- Plans for the Use and Dissemination of Foreground Knowledge;

Concept and Project Objectives

- Challenge, e.g.: effective use of multicore systems;
- Vision, e.g.: new structured design;
- Aims - high level/main objectives, e.g.: new design patterns;
- Objectives used in wp-s, e.g. efficient parallel implementations - with detailed description,

Progress Beyond the State-of-the-Art, Success Criteria

- List and detailed description of results beyond the state-of-the-art;
- List of success criteria related to objectives, e.g. working software tools / benchmarks / validation methods
- Success criteria achived by MS and reported in deliverables;

S/T Methodology and Associated Work Plan

- Structure and dependencies of work packages;
- Objectives and the corresponding work packages;
- Risks and Contingency Plans;
- Timing and dependecies (wp-s, tasks) - Gant chart;
- Critical Path Analysis;

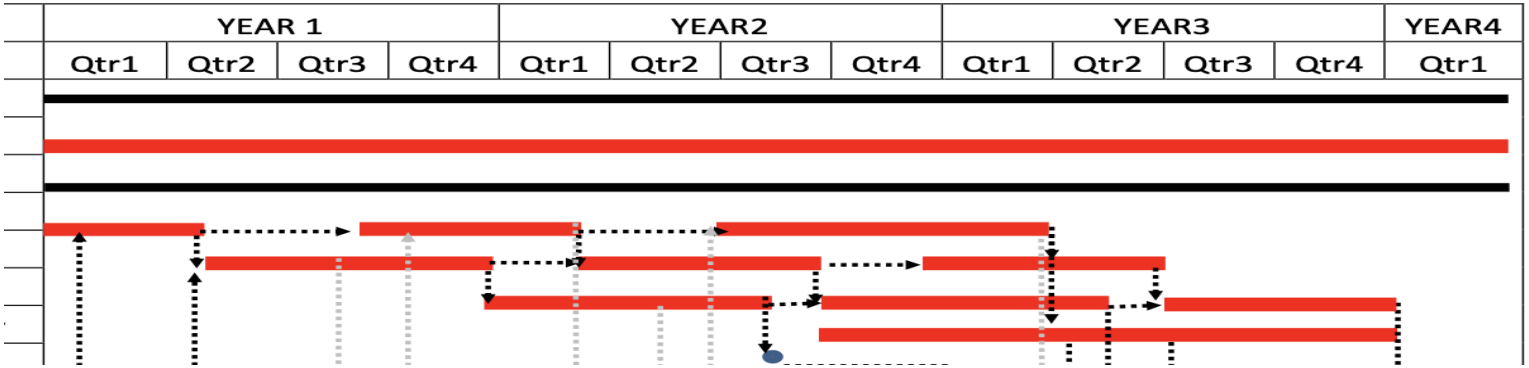

	Start Month	End Month	Max. Slack	Depends on
	1	23	8	T6.2 (M2), T6.4
	4	30	4	T2.1 (M4, M14,
	12	36	4	T2.2 (M12, M23,

Management Structure and Procedures

- Steering Committee;
- Advisory Board;
- Work Package Team Leaders;
- Project Coordinator, Administrator - Project Management Expertise;
- Beneficiaries - Principal Investigators;
- Consortium as a Whole - Areas of Beneficiary Expertise;
- Budget justification;
- Management costs justification;

Impact, Dissemination and Exploitation

- List of expected impacts - related to aims - and how impact will be achived;
- E.g.: European leadership in cross-cutting technologies ..;
- Dissemination, e.g. via education, user communities, conferences;
- List of expected publications;
- Communication plan;
- Innovation, exploitation, business plan, competitor analysis;
- Intellectual properties (IP), backgorund and foreground knowledge;
- List of expected fg. IP-s, protection, patents;
